



# Main Street Reconstruction Project 2017

## 3-Week Look Ahead

Main Street  
Project 2017

Phase I  
Hwy LL to  
Beech St

**PROJECT  
FIELD OFFICE**

At the Mobil  
Gas Station  
on corner of  
CTH LL and  
Main Street.

**Field Office  
Hours:**  
7am - 5pm  
Mondays  
thru Fridays


**Field Office  
Phone#:**  
920-323-2876

### Week of October 31<sup>st</sup>

The 1<sup>st</sup> lift of asphalt has been started on Monday. It will be placed from Hwy LL all the way to Beech Street, and is expected to last 3 days.

Meanwhile, placement of topsoil and sod along the terrace will restart on Tuesday or Wednesday and continue through the end of the week.

The concrete work for driveway aprons and sidewalks is expected to be completed by the end of this week.

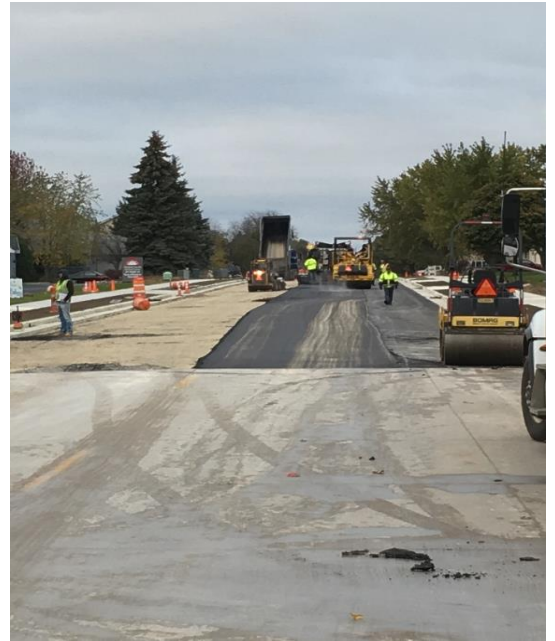

### Week of November 6<sup>th</sup>

Landscaping of the terrace will continue on Monday with continued placement of topsoil and sod.

The 2<sup>nd</sup> lift of asphalt is scheduled to be placed Tuesday, Wednesday and Thursday of the week of November 6<sup>th</sup>.

### Week of November 13<sup>th</sup>

Striping of the newly asphalted street is planned for Monday and Tuesday of the week of November 13<sup>th</sup>.

Landscaping of the terrace with topsoil and sod will continue, and sign replacement will start.

If the new light poles are available at this time, they will start being installed on the concrete bases.

